QUARTERLY PROJECT REPORT

July 1, 2020 – September 30, 2020



Coast Community College District **Program Summary**

Closed Projects
CCC College Center Restroom Renovation
CCC Energy Efficiency Projects
CCC Le-Jao Student Resource Center
CCC GG Center Solar P/V Carport System
GWC Campus Safety/Community Education Building & Campus Entry
GWC Elevator Repairs/Replacement
GWC Rehabilitation Center Remodel
GWC Campus-wide Wayfinding/Signage
GWC Math & Science Improvements
GWC MDF/Communications Relocation
GWC Technology Projects
GWC Security & Access Infrastructure
GWC Criminal Justice Training Center
GWC Security & Access Infrastructure

Closed Projects (cont.)
OCC IDC Phase I (Business, Math, Computing Center)
OCC Clark Center
OCC Energy Efficiency Projects
OCC Planetarium
OCC Solar PV/Adams Parking Lot Improvements
OCC Recycling Center
OCC Legacy Hall
OCC Watson Hall Renovation
OCC Technology Projects
OCC Securitization Fund
OCC Sustainable Landscape Improvements

Financial Closing CCC Newport Beach Student Support Center **GWC Math/Science Building OCC Watson Hall**

Coast Community College District **Program Summary**

Pro	iects	ln (Const	truction

CCC Student Services Center

OCC Student Union Complex

OCC Adaptive PE, Gym & Pool

OCC Language Arts/Social Sciences Building

OCC Maritime Academy Expansion

Projects In Design

GWC Language Arts Complex

OCC Watson Hall Improvements

Other Ongoing Projects

CCC Technology Projects

DIST Technology Projects

GWC Energy Efficiency Projects

GWC Classroom Improvement Projects

OCC Westside Planning Projects



Coast Community College District **Program Summary**

State Funded Project Proposals

GWC Fine Arts Renovation

GWC Technology Project

OCC Chemistry Building

OCC Skills Center Renovation/Replacement

Budgeted Projects

CCC Garden Grove Center Renovation

Planned Projects

CCC Le-Jao Parking Expansion

GWC Technology Building Improvements

GWC Business/Social Sciences Building

GWC Cosmetology

GWC Central Plant Warehouse

OCC Performing Arts/Dance

OCC Parking Structure



Coast Community College District Split Budget Summary

Project	Total Budget	Non-Measure M	Measure M
CCC EE – GG Ctr. Boiler	\$1,270,525	\$512,011	\$758,514
GWC Language Arts Complex	\$54,648,000	\$20,331,000	\$34,317,000
GWC Criminal Justice Training Center	\$27,765,999	\$900,000	\$26,865,999
GWC EE – Exterior Lighting Retrofit	\$513,409	\$505,914	\$7,495
GWC EE – Interior Lighting Retrofit	\$432,088	\$422,013	\$10,075
OCC Language/Social Science Building	\$68,919,000	\$31,221,000	\$37,698,000
OCC Maritime Academy Expansion	\$22,095,000	\$500,000	\$21,595,000
OCC EE – Exterior Lighting Retrofit	\$1,369,092	\$679,189	\$689,903
OCC SL – Landscape Improvements	\$1,008,000	\$125,000	\$883,000
OCC EE – Campus Sub-metering Project	\$1,311,306	\$634,000	\$677,306
TOTALS	\$157,237,419	\$55,330,127	\$101,907,292



Coastline College Newport Beach Student Support Center

Current Phase: Financial Closing

Architect: LPA

Contractor: Astra Builders

Construction Manager: Randy Flint

Scope: Installation of exterior shade structures to enhance

student study areas and learning environment



Newport Beach Student Support Center

BUDGET

	Budget	Quarter Expenses	Total Expended	Balance Remaining
Construction	\$800,000	\$34,604	\$692,082	\$107,918
Soft Cost	\$163,000	\$0	\$9,943	\$153,057
FFE/IT	\$0	\$0	\$0	\$0
Contingency	\$48,000			\$48,000
TOTAL	\$1,011,000	\$34,604	\$702,025	\$308,975

SCHEDULE

	Start
Design	January 2016
Plan Review	February 2016
Bidding	May 2017
Construction	August 2017
Project Completion	September 2019
Closeout	August 2020

Status Update: Final retention payment complete. DSA Fee's have been paid and project closed this quarter.



Coastline College **Student Services Center**

Current Phase: In Design

Architect: Westgroup Designs

Contractor: Multi-Prime

Construction Manager: C.W. Driver

Scope: Construction of a 53,000 sf student services center to house Admissions & Records, Financial Aid, Veterans Resource Center, EOPS, Counseling, Student Life, Library Office, Extended Learning, Business Office, Marketing, Public Safety, Research, Foundation, Instructional Services, Human Resources and Administration. Students will be served by a one stop front counter with staff from multiple departments in peak times of the year



Coastline College **Student Services Center**







Coastline College Student Services Center

BUDGET

	Budget	Quarter Expenses	Total Expended	Balance Remaining
Construction	\$27,600,853	\$87,559	\$521,987	\$27,078,866
Soft Cost	\$4,101,000	\$54,277	\$2,025,350	\$2,075,650
FFE/IT	\$1,911,000	\$0	\$112,341	\$1,798,659
Contingency	\$1,307,000			\$1,307,000
TOTAL	\$34,919,853	\$141,836	\$2,659,678	\$32,260,175

SCHEDULE

StartDesignSeptember 2017Plan ReviewMarch 2020BiddingAugust 2020ConstructionOctober 2020Project CompletionJuly 2022CloseoutAugust 2022

Status Update: DSA approved plans have been received, Bookstore demolition is complete and scope review with apparent low bidders is ongoing. Construction to begin in October.



Coastline College **Technology Projects**

TOTAL ALLOCATION: \$3,195,351

Project	Budget	Quarter Expenses	Total Expended	Balance Remaining
TECH – Classroom Technology Upgrades	\$1,598,286	\$0	\$1,400,015	\$198,271
TECH – IT Infrastructure Improvements	\$1,197,065	\$0	\$1,197,065	\$0
TECH – Student Kiosks, Wayfinding Signages	\$400,000	\$0	\$286,925	\$113,075
Totals	\$3,195,351	\$0	\$2,884,005	\$311,346



Golden West College Math & Science Building

Current Phase: Financial Closing

Architect: HMC Architects

Contractor: Multiple Prime

Construction Manager: Sundt Construction

Scope: Construction includes a new 122,747 square foot Math/Science facility. This project includes the demolition of the old Trade-Industry 2 building complex as well as the adjacent child care facility. The new 3 story facility will replace the existing Math/Science building and include lecture, lab, computer lab and support space for Math, Life Science and Physical Science departments, as well as a STEM Center.



Golden West College Math & Science Building





Golden West College Math & Science Building

BUDGET

	Budget	Quarter Expenses	Total Expended	Balance Remaining
Construction	\$61,550,422	\$1,156,724	\$61,352,993	\$197,429
Soft Cost	\$11,933,000	\$52,632	\$11,322,687	\$610,313
FFE/IT	\$5,562,000	\$9,581	\$3,698,743	\$1,863,257
Contingency	\$722,115			\$722,115
TOTAL	\$79,767,537	\$1,218,937	\$76,374,423	\$3,393,114

ш
る
<u></u>
Š
S

	Start
Design	January 2015
Plan Review	February 2016
Bidding	November 2016
Construction	June 2017
Project Completion	August 2019
Closeout	May 2020

Status Update: Submitting closeout documents to DSA for certification. Trade contract packages have been reconciled and retention payments are being issued.



Golden West College Language Arts Complex

Current Phase: In Design

Architect: HMC Architects

Contractor: Multiple Prime

Construction Manager: Sundt Construction

Construction of a new three-story 65,500 square foot instructional facility to replace 60 year old social sciences classrooms and 50 year old literature and languages building



Golden West College Language Arts Complex











Golden West College Language Arts Complex

,	
1	
9	
-	
•	١

	Budget	Quarter Expenses	Total Expended	Balance Remaining
Construction	\$40,072,000	\$27,578	\$213,339	\$39,858,661
Soft Cost	\$8,167,000	\$127,722	\$1,214,366	\$6,952,634
FFE/IT	\$3,807,000	\$0	\$0	\$3,807,000
Contingency	\$2,602,000			\$2,602,000
TOTAL	\$54,648,000	\$155,300	\$1,427,705	\$53,220,295

SCHEDULE

	Start	
Design	August 2018	
Plan Review	August 2019	
Bidding	November 2020	
Construction	January 2021	
Project Completion	December 2022	
Closeout	March 2023	

Status Update: Contractor prequalification process has concluded. Construction drawings have been submitted to the State Chancellors office for the next increment of funding. Construction expected to start late January.



Classroom Improvement Projects

TOTAL ALLOCATION: \$2,945,266

Project	Budget	Quarter Expenses	Total Expenses	Balance Remaining
CI - General Classroom Improvements	\$2,181,344	\$100,406	\$2,107,905	\$73,439
CI – Classroom Seating	\$158,935	\$0	\$158,935	\$0
CI – Math & Science Renovation	\$445,716	\$0	\$445,716	\$0
CI - Theater Refurbishment	\$159,271	\$0	\$159,271	\$0
Totals	\$2,945,266	\$100,406	\$2,871,827	\$73,439



Golden West College Energy Efficiency Projects

TOTAL ALLOCATION: \$1,609,073

Project	Budget	Quarter Expenses	Total Expended	Balance Remaining
EE – Energy Efficiency Upgrades	\$17,570	\$0	\$17,570	\$0
EE – Central Plant Expansion	\$875,633	\$0	\$869,299	\$6,334
Totals	\$893,203	\$0	\$869,299	\$6,334



Orange Coast College Maritime Academy Expansion

Current Phase: In Construction

Architect: HPI Architecture


Contractor: Multiple Prime

Construction Manager: TELACU

Scope: Increment I: New construction of a 10,000 square foot training and classroom facility with 37 parking spaces. Increment II: Pedestrian bridge connecting to Sailing Center across Pacific Coast Highway and ADA upgrades to the existing facility.



Orange Coast College Maritime Academy Expansion

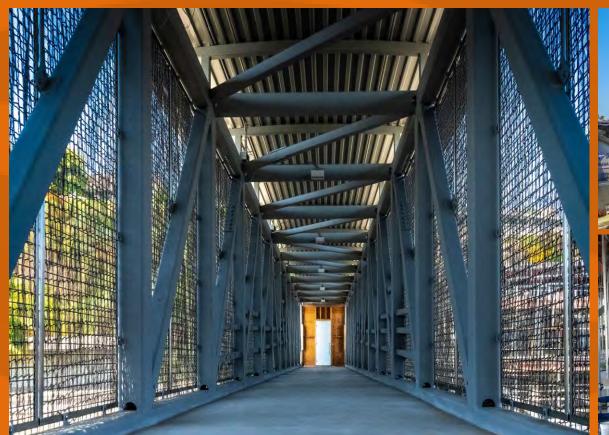



Orange Coast College Maritime Academy Expansion

BUDGET

Budget Quarter Expenses Total Expended Balance Construction \$12,026,082 \$17,173,000 \$1,927,458 \$5,146,918 Soft Cost \$2,700,000 \$3,832,708 \$348,819 (\$1,132,708) FFE/IT \$1,473,000 \$0 \$3,821 \$1,469,179 Contingency \$249,000 \$249,000 **TOTAL** \$21,595,000 \$2,276,276 \$15,862,610 \$5,732,390

SCHEDULE

Start
December 2007
August 2017
February 2019
April 2019
April 2021
June 2021

Status Update: New elevator installation ongoing. Remodel of existing Sailing Center lobby ongoing. Roofing, interior framing and drywall installation has commenced.

*Soft Costs, which includes construction management, architectural design, testing & inspections, and surveying, have exceeded the allocated budget due to an increase in the total hard construction amount (professional services are typically a percentage of the total hard cost).



Orange Coast College **Student Union Complex**

Current Phase: In Construction

Architect: tBP Architecture

Contractor: Multiple Prime

Construction Manager: C.W. Driver


Scope: The new 160,000 SF Student Union will serve as a hub for student activities and socialization. Situated along Fairview Road, the new 2-building complex will house essential programs to the college campus, including student activities, food services, conference center, and other support programs. Post construction, the existing administration building will be remodeled to house additional services.



Orange Coast College **Student Union Complex**





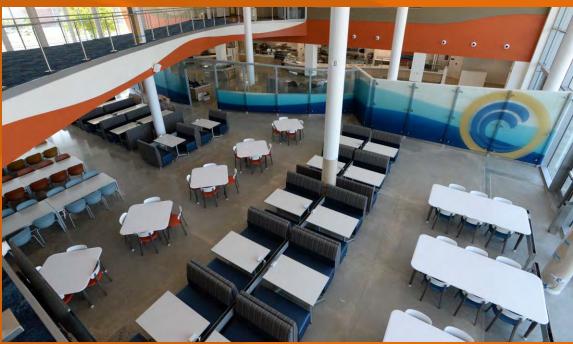

Orange Coast College Student Union Complex

BUDGET

Total Expended Balance Remaining Budget Quarter Expenses Construction \$90,954,483 \$2,644,691 \$85,786,324 \$5,168,159 **Soft Cost** \$12,900,000 \$512,724 \$11,616,236 \$1,283,764 FFE/IT \$8,641,000 \$3,005,757 \$3,521,459 \$5,119,541 Contingency \$909,545 \$909,545 **TOTAL** \$113,405,028 \$6,163,172 \$100,924,019 \$12,481,009

SCHEDULE

	Start
Design	September 2016
Plan Review	May 2018
Bidding	July 2018
Construction	August 2018
Project Completion	August 2020
Closeout	January 2021

Status Update: Final furniture solution installation ongoing. Former Administration and new Campus Safety building remodel has begun while quad sitework continues.



Orange Coast College Kinesiology / Adaptive PE / Aquatics

Current Phase: In Construction

Architect: tBP Architects

Contractor: Multiple Prime

Construction Manager: C.W. Driver

Scope: Increment I: New Kinesiology/Athletics Phase I project will include a 65 meter competition pool, a 25 meter instructional pool, Kinesiology/Athletics Division office, equipment management, Adaptive PE fitness & aerobics studios, team rooms/locker rooms, and support spaces. Increment II: Upgrades to the existing locker room to consolidate space for the existing gymnasium functions.



Orange Coast College Kinesiology / Adaptive PE / Aquatics





Orange Coast College

Kinesiology / Adaptive PE / Aquatics

П	
G	
Ŏ	
፳	

	Budget	Quarter Expenses	Total Expended	Balance Remaining
Construction	\$41,130,395	\$1,489,231	\$40,564,657	\$565,738
Soft Cost	\$6,100,000	\$113,186	\$6,054,784	\$45,216
FFE/IT	\$3,907,000	\$359,601	\$756,849	\$3,150,151
Contingency	\$211,304			\$211,304
TOTAL	\$51,348,699	\$1,962,018	\$47,376,290	\$3,972,409

SCHEDULE

	Start
Design	January 2017
Plan Review	October 2018
Bidding	October 2018
Construction	November 2018
Project Completion	March 2020
Closeout	December 2020

Status Update: Project is complete and project team is working to close out trade packages.



Orange Coast College Language Arts/Social Sciences Building

Current Phase: In Design

Architect: tBP Architects

Contractor: Multiple Prime

Construction Manager: C.W. Driver

Construction of a new 100,000 square foot, 3 story instructional facility to replace 60 year old social sciences classrooms and 50 year old literature and languages building. A new skyway bridge will connect the new building to the existing MBCC.



Orange Coast College Language Arts/Social Sciences Building





Language Arts/Social Sciences Building

I		
ľ		
(j	,
2		
)
•	•	

	Budget	Quarter Expenses	Total Expended	Balance
Construction	\$27,722,864	\$6,923,067	\$29,535,995	(\$1,813,131)
Soft Cost	\$5,181,656	\$502,211	\$4,659,129	\$522,527
FFE/IT	\$2,626,099	\$0	\$10,273	\$2,615,826
Contingency	\$2,167,381			\$2,167,381
TOTAL	\$37,698,000	\$7,425,278	\$ 34,205,397	\$3,492,603

SCHEDULE

	Start
Design	October 2017
Plan Review	May 2021
Bidding	August 2019
Construction	October 2019
Project Completion	April 2021
Closeout	June 2021

Status Update: Roofing installation is finished. Exterior finishes is roughly 30% complete and on schedule. Interior framing has commenced.



^{*}Language Arts and Socials Sciences is a 50/50 state funded project. Negative construction balance is a result of Measure M absorbing all expenses, with 50% to be reimbursed by Proposition 51 funds.

Orange Coast College Watson Hall Improvements

Current Phase: Financial Closing

Architect: OCC Measure M Team

Contractor: N/A

Construction Manager: OCC Measure M Team

Scope: Re-purposing of Watson Hall to provide improved integration of student services, upgrades to wayfinding in both interior and exterior applications, increase of workstation areas to support additions to staffing, and the incorporation of queuing & student waiting areas.



Orange Coast College Watson Hall Improvements

Į	į	,
		ì
)
		ì

	Budget	Quarter Expenses	Total Expended	Balance Remaining
Construction	\$432,238	\$0	\$64,705	\$367,533
Soft Cost	\$86,000	\$0	\$1,064	\$84,936
FFE/IT	\$115,000	\$3,358	\$113,191	\$1,809
Contingency	\$12,000			\$12,000
TOTAL	\$645,238	\$3,358	\$178,960	\$466,278

SCHEDULE

	Start
Design	August 2015
Plan Review	N/A
Bidding	N/A
Construction	October 2016
Project Completion	July 2021
Closeout	August 2021

Status Update: Furniture solutions at all designed areas complete. In the process of financial closing.



Orange Coast College Westside Planning Projects

TOTAL ALLOCATION: \$1,658,000

Project	Budget	Quarter Expenses	Total Expended	Balance Remaining
WP - Skill Center & Technology Center Improvements	\$750,000	\$0	\$508,319	\$241,681
WP - New Classroom & Teaching Spaces	\$850,000	\$0	\$0	\$850,000
WP - Horticulture Improvements	\$58,000	\$0	\$44,147	\$13,853
Totals	\$1,658,000	\$0	\$552,466	\$1,105,534



District **Technology Projects**

TOTAL ALLOCATION: \$6,097,231

Project	Budget	Quarter Expenses	Total Expended	Balance
TECH - Active Dir, Exchange and SharePoint	\$977,646	\$0	\$977,646	\$0
TECH - Appl Software for International Students	\$342,500	\$0	\$342,500	\$0
TECH - Banner Upgrades	\$999,384	\$0	\$999,384	\$0
TECH - Enterprise VDC & Server Consolidation	\$147,897	\$0	\$144,466	\$3,431
TECH - Helpdesk Software	\$34,630	\$0	\$34,630	\$0
TECH – Microsoft Exchange, Email & Archiving	\$304,008	\$845	\$198,541	\$105,467
TECH - VoIP Conversion	\$754,305	\$0	\$754,305	\$0
TECH – MDF/Communications Relocation	\$1,013,385	\$0	\$1,013,385	\$0
Totals	\$4,573,755	\$845	\$4,464,857	\$108,898



\$19,997,513

Total Quarterly Expenses

\$487,094,672

Total Expenses From Inception

69.78%

Percentage Expended

